




2016 COMBINED SEWER IMPROVEMENTS CONSTRUCTION STATUS REPORT

Status Report #4, May 6, 2016

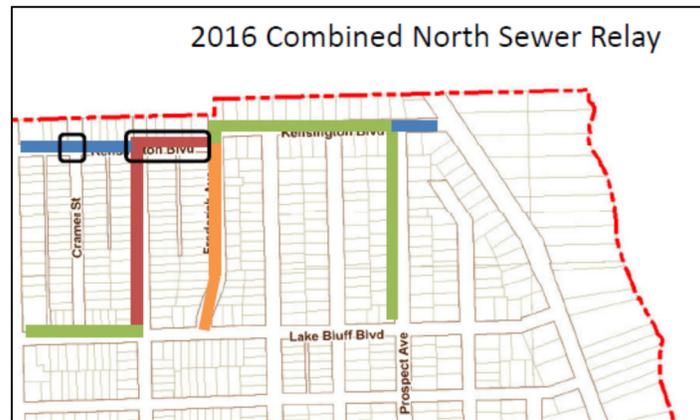

This Status Report will provide an update on the 2016 Combined Sewer Improvements recent and upcoming work.

WORK COMPLETED FROM May 2nd, 2016 THROUGH May 6th, 2016

Globe has completed water main work throughout the project. There is still the possibility of water main shutdowns during the project. Globe continued installing sanitary sewer along N. Prospect Avenue.

WORK SCHEDULED FOR THE WEEK OF May 9nd, 2016

Globe will continue installation of sanitary sewer along N. Prospect Avenue and likely reach E. Kensington Boulevard and begin installing sanitary sewer along E. Kensington Boulevard. Globe will begin sanitary sewer installation at N. Oakland Avenue and E. Lake Bluff Boulevard working east to N. Murray Avenue. Traffic and parking restrictions in this area will be in effect for approximately 3 weeks until sewer and concrete restoration work is completed in the Oakland/Lake Bluff intersection.

If you have any questions or special needs please feel free to contact one of the following:

Phil Bzdusek, Project Manager - 414-305-9740
Colin Doherty, Onsite Representative - 608-658-9508

Shorewood DPW 414-847-2650
www.villageshore.org
