




# 2016 COMBINED SEWER IMPROVEMENTS CONSTRUCTION STATUS REPORT

Status Report #11, June 24, 2016

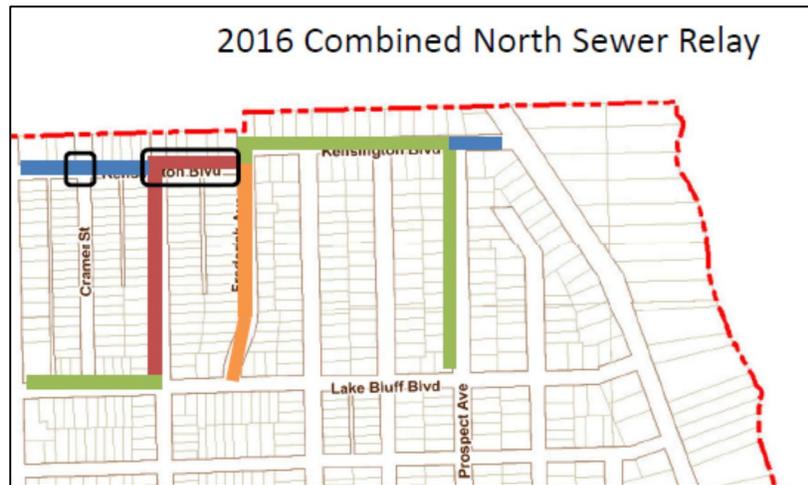

This Status Report will provide an update on the 2016 Combined Sewer Improvements recent and upcoming work.

## **WORK COMPLETED FROM June 20, 2016 THROUGH June 24, 2016**

Globe finished installing mainline sanitary sewer along E. Murray Avenue. Globe began installing sanitary sewer along E. Kensington Boulevard. Globe completed removals on N. Frederick Avenue. Pieper Electric installed street lighting wire and conduit.

## **WORK SCHEDULED FOR THE WEEK OF June 27, 2016**

Globe will continue installing sanitary sewer along E. Kensington Boulevard. Globe will begin installing sanitary sewer laterals along E. Murray Avenue. Globe may install porous paving trenches and piping at the intersection of E. Kensington Boulevard and N. Frederick Avenue.

Curb and gutter work on N. Frederick Avenue is scheduled for the week of July 5<sup>th</sup>.

***Driveway access will be unavailable for approximately 10 days when curb and gutter and driveways are installed. During removals driveway access may be unavailable for 1 day.***

If you have any questions or special needs please feel free to contact one of the following:

Phil Bzdusek, Project Manager - 414-305-9740  
Colin Doherty, Onsite Representative - 608-658-9508

Shorewood DPW 414-847-2650  
[www.villageshore.org](http://www.villageshore.org)
