




2020 ROAD RECONSTRUCTION PROGRAM CONSTRUCTION STATUS REPORT

Status Report #3, May 1, 2020
Shorewood, WI
Contract 1-2020

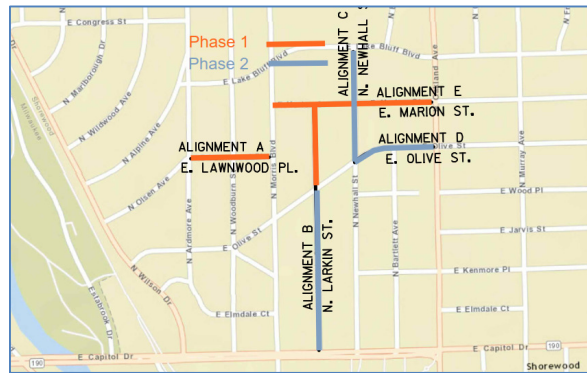

This Status Report will provide an update on the 2020 Road Reconstruction Program's recent and upcoming work.

WORK COMPLETED FROM April 27th, 2020 THROUGH May 1st, 2020

Stark completed removals and installed aggregate base on East Marion Street from North Morris Boulevard to North Newhall Street. Stark completed installation of aggregate base on East Lawnwood Place. UPI replaced water valves and hydrants throughout the project area. Interstate Tree Company completed tree removals and stump grinding throughout the project area.

WORK SCHEDULED FOR THE WEEK OF May 4th, 2020

Stark plans to begin removals and install aggregate base on East Marion Street, beginning at North Oakland Avenue and working toward North Newhall Street. **Stark plans to install curb and gutter, driveways, and sidewalks on East Lawnwood and along East Marion Street from North Morris Boulevard to North Newhall Street. Residents will have no access to driveways during curb and gutter and driveway installation for approximately 10 days.** UPI plans to complete replacement of water valves along the 4200 block of North Larkin Street. **Temporary water service shutdowns will occur along this block and potentially adjacent blocks that will last for several hours.**

The Village will notify residents of the shutdowns and provide bottled water. If you have any questions or special needs please feel free to contact one of the following:

- Phil Bzdusek, Project Manager: (414) 305-9740
- Isak Fruchtmann, Onsite Representative: (952) 688-3435
- Shorewood DPW: (414) 847-2650
