




2022 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

Status Report #12, July 29, 2022



Alley 3 Storm Sewer

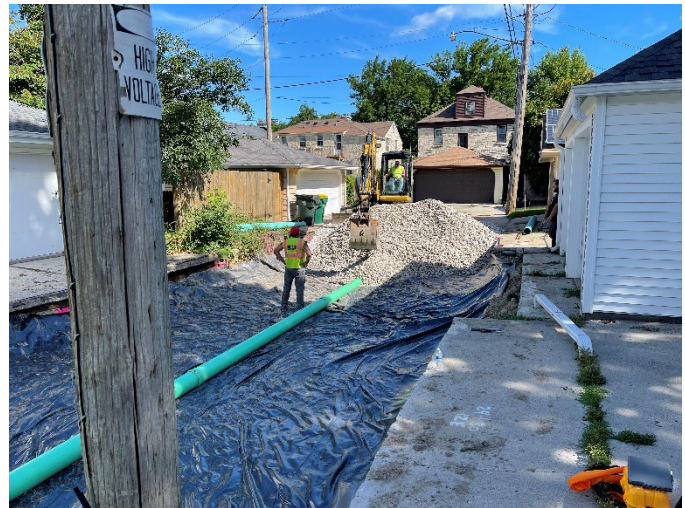

Alley 3 Storm Sewer

This Status Report will provide an update on the 2022 Alley Reconstruction Project's recent and upcoming work.

WORK COMPLETED WEEK OF July 25th

Lalonde completed excavation and removals of the east and south leg of Alley 3. Sirrah finished storm sewer installation on the east leg of Alley 3.

WORK SCHEDULED WEEK OF August 1st

Lalonde plans to finish excavation of Alley 3 on the north leg. Sirrah plans to continue storm sewer installation.

Alley 6 is scheduled to begin the week of August 8th. Construction notices will be given out prior to the beginning of construction.

To ensure timely collection of refuse and recycling, residents are reminded to place carts at the curb by 7 AM on their normal collection day.

If you have any questions or special needs, please feel free to contact one of the following: Robbie Maas, Village's Onsite Representative – 262-893-4202 Or Shorewood DPW 414-847-2650

www.villageofshorewood.org/2022alleys
