




2022 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

Status Report #16, September 2, 2022



Alley 3 Concrete

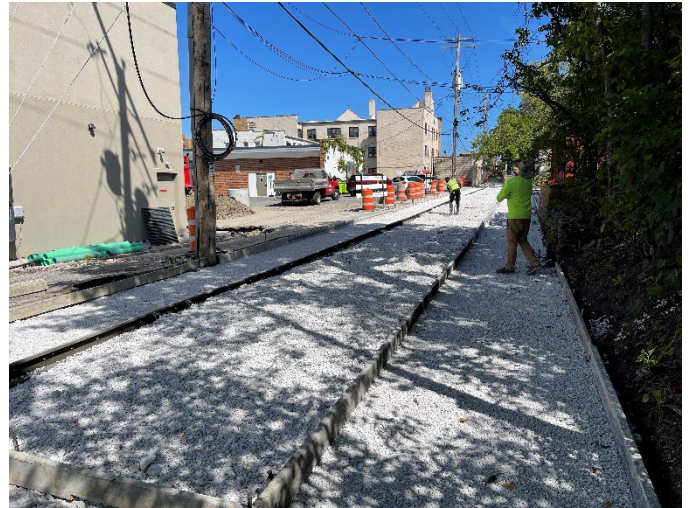

Alley 6 Concrete Forms

This Status Report will provide an update on the 2022 Alley Reconstruction Project's recent and upcoming work.

WORK COMPLETED WEEK OF August 29th

Lalonde finished grading for concrete on Alley 3 and Alley 6. Lalonde poured the concrete headers for Alley 3 and Alley 6.

WORK SCHEDULED WEEK OF September 5th

No work will be performed for Labor Day (September 5).

Lalonde will grade for Paver installation on Alley 3 and Alley 6. Breckenridge will install the pavers.

Lalonde will begin removals and grading on Alley 4.

Lalonde will sawcut the pavement on Alley 8 and Alley 9. No other work will be done on these alleys week of September 5th.

To ensure timely collection of refuse and recycling, residents are reminded to place carts at the curb by 7 AM on their normal collection day.

If you have any questions or special needs, please feel free to contact one of the following:
Robbie Maas, Village's Onsite Representative – 262-893-4202 Or Shorewood DPW 414-847-2650 www.villageofshorewood.org/2022alleys
