




2020 ROAD RECONSTRUCTION PROGRAM CONSTRUCTION STATUS REPORT

Status Report #12, July 2, 2020

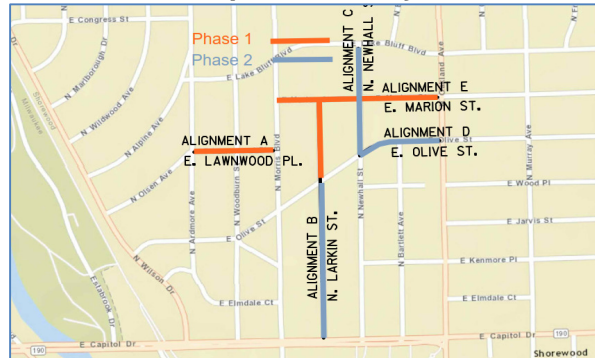

This Status Report will provide an update on the 2020 Road Reconstruction Program's recent and upcoming work.

WORK COMPLETED FROM June 29th, 2020 THROUGH July 2nd, 2020

The contractor is restricted from working on July 3rd due to the Holiday weekend.

Phase 2 Construction

The contractor completed removals and installation of aggregate base on North Newhall Street. The contractor installed topsoil in the terrace areas along North Larkin Street between East Olive Street and East Capital Drive. The electrical contractor installed pull boxes on North Larkin Street between East Olive Street and East Capital Drive, as well as street lighting conduit at the intersection of North Newhall Street and East Marion Street.

Phase 1 Construction

Landscape contractor watered newly installed sod.

WORK SCHEDULED FOR THE WEEK OF July 6th, 2020

Phase 2 Construction

The contractor plans to begin installing curb and gutter, driveways, and sidewalk ramps on July 7th along East Olive Street and North Newhall Street. The electrical contractor plans to install street lighting wire along North Larkin Street between East Olive Street and East Capital Drive. **Property Owners along East Olive Street and North Newhall Street will not have access to driveways for approximately 10 days after curb and gutter, and driveways are installed.**

Phase 1 Construction

Landscape contractor will continue to water installed sod.

PLEASE BE AWARE: Temporary streetlight outages will occur during the construction process. All efforts will be made to limit the duration the streetlights remain out.

If you have any questions or special needs, please feel free to contact one of the following:

- Phil Bzdusek, Project Manager: (414) 305-9740
- Isak Fruchtmann, Onsite Representative: (952) 688-3435
- Shorewood DPW: (414) 847-2650

www.villageofshorewood.org/2020Roads

www.villageofshorewood.org/NotifyMe
