




2020 ROAD RECONSTRUCTION PROGRAM CONSTRUCTION STATUS REPORT

Status Report #14, July 17, 2020

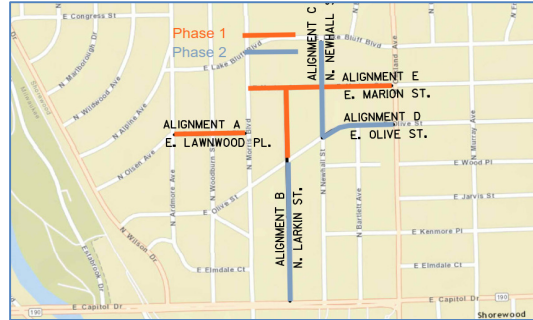

This Status Report will provide an update on the 2020 Road Reconstruction Program's recent and upcoming work.

WORK COMPLETED FROM July 13th, 2020 THROUGH July 17th, 2020

Phase 2 Construction

The contractor installed driveway aprons, sidewalk, and carriage walks along East Olive Street and North Newhall Street. The contractor completed fine grading and installation of the binder layer of asphalt pavement along East Olive Street and North Newhall Street. The electrical contractor completed installation of street lighting wiring throughout the project area.

Phase 1 Construction

No work was completed.

WORK SCHEDULED FOR THE WEEK OF July 20th, 2020

Phase 2 Construction

The contractor plans to complete installation of sidewalks, carriage walks, and curb ramps throughout the project area. The contractor plans to install topsoil in terrace areas along North Newhall Street and East Olive Street. The contractor may install sod in terrace areas.

Property Owners along North Newhall Street and East Olive Street will not have access to driveways until Tuesday, July 21st or Wednesday, July 22nd. Driveways will have caution tape across the driveways and cones at driveways that will be removed when access is permitted.

Phase 1 Construction

No work is planned.

PLEASE BE AWARE: Temporary streetlight outages will occur during the construction process. All efforts will be made to limit the duration the streetlights remain out.

Sod has been installed in various locations. The contractor is required to water the sod for 30 days after installation, however any sod watering completed by residents to assist the contractor is appreciated.

If you have any questions or special needs, please feel free to contact one of the following:

- Phil Bzdusek, Project Manager: (414) 305-9740
- Isak Fruchtmann, Onsite Representative: (952) 688-3435
- Shorewood DPW: (414) 847-2650
